




Phase 1 Construction

- Demo traffic signal at 29th Avenue & Fenton Street Intersection
 - Keep one lane of 29th Avenue and Fenton Street open at all times
 - Install temporary stop signs on Fenton Street
- Install sanitary sewer west of Gray Street
 - Keep south lane of 29th Avenue open at all times
 - 29th Avenue can be closed for 24 hours for the connection to the existing manhole at Station 10+25




Phase 2 Construction

- Construct north half of 29th Avenue between 6121 and 5795 29th Avenue
 - Keep south lane of 29th Avenue open at all times
 - Maintain driveway access to 6121, 5995, 5837, and 5861 29th Avenue and Ashland Reservoir

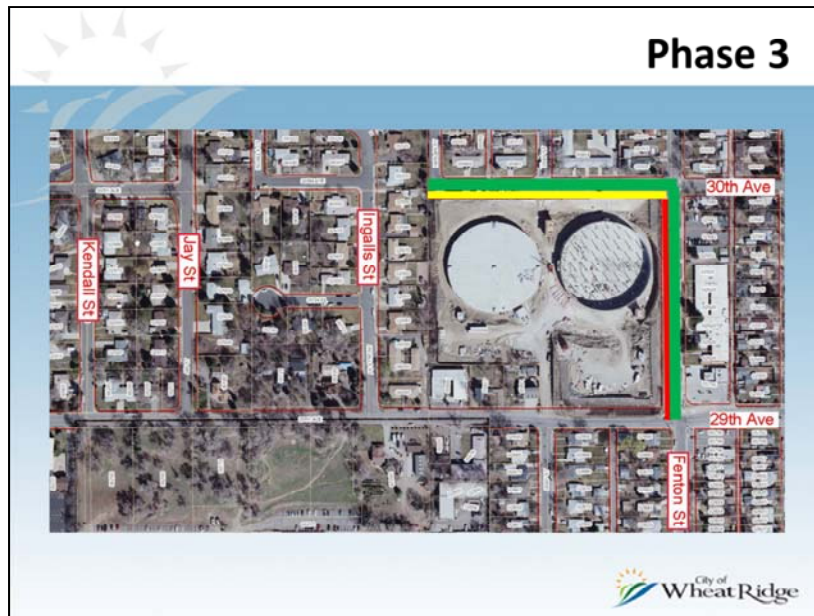


Phase 3 Construction – This phase can be done during Phase 2, 4, or 5

- Phase 3.1 – Construct streetscape improvements along the west side of Fenton Street
 - Keep east lane of Fenton Street open at all times
 - Parking on west side of Fenton Street moved to south side of 30th Avenue
- Phase 3.2 – Construct streetscape improvements along the south side of 30th Avenue
 - Keep north lane of 30th Avenue open at all times
 - These improvements can be started after the parking on the west side of Fenton Street has been restored
- Phase 3.3 – Mill and overlay 30th Avenue and Fenton Street
 - Mill and overlay 30th Avenue
 - Mill and overlay Fenton Street
 - Parking on Fenton Street moved to south side of 30th Avenue and north side of 29th Avenue east of Fenton Street

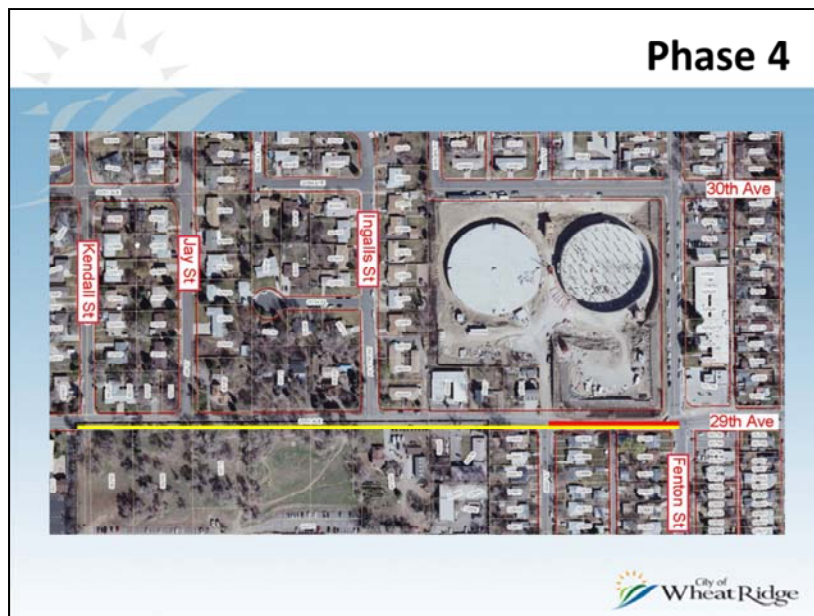


Phase 4 Construction

- Install sanitary sewer between Gray and Fenton Streets
 - Start at Gray Street and work east
 - Complete sanitary sewer construction before water line construction reaches Gray Street
- Install water line between Kendall and Fenton Streets
 - Start at Kendall Street and work east
- Keep north lane of 29th Avenue open at all times

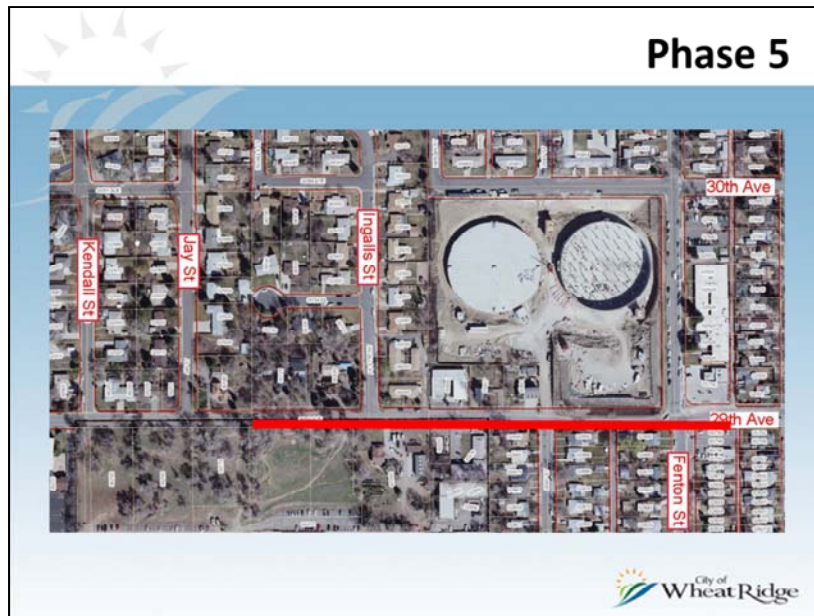

Phase 5 Construction

- Construct south half of 29th Avenue between 6121 and 5795 29th Avenue
 - Keep north lane of 29th Avenue open at all times
 - Maintain driveway access to 6028, 6000, and 5978 29th Avenue

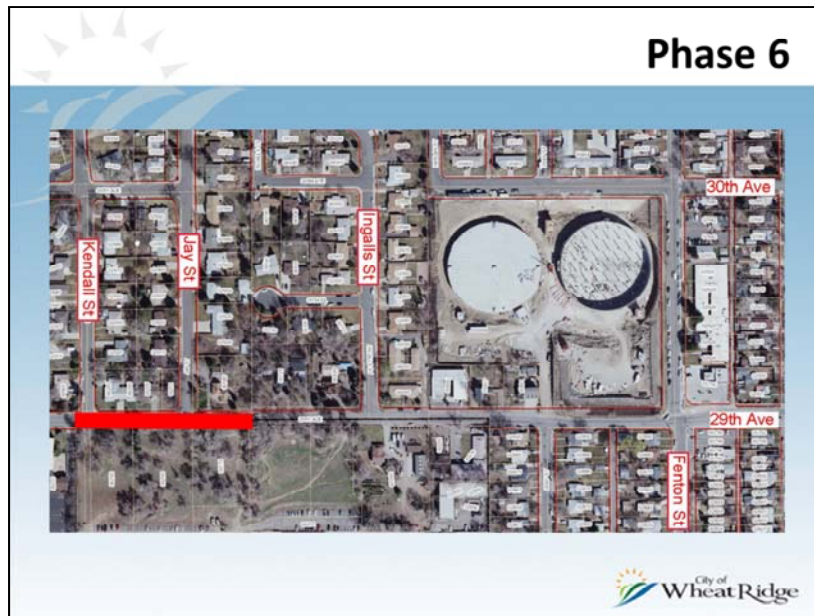

Phase 6 Construction

- Construct 29th Avenue between Kendall Street and 6185 29th Avenue
 - Close 29th Avenue between Kendall Street and 6185 29th Avenue
 - Detour traffic on 29th Avenue at Pierce and Fenton Streets
